

Modernization Planning

**Mr. Tom Gibson,
SHIPS-F**


9 June 2004



USS CURTIS WILBUR (DDG 54) SRA





5

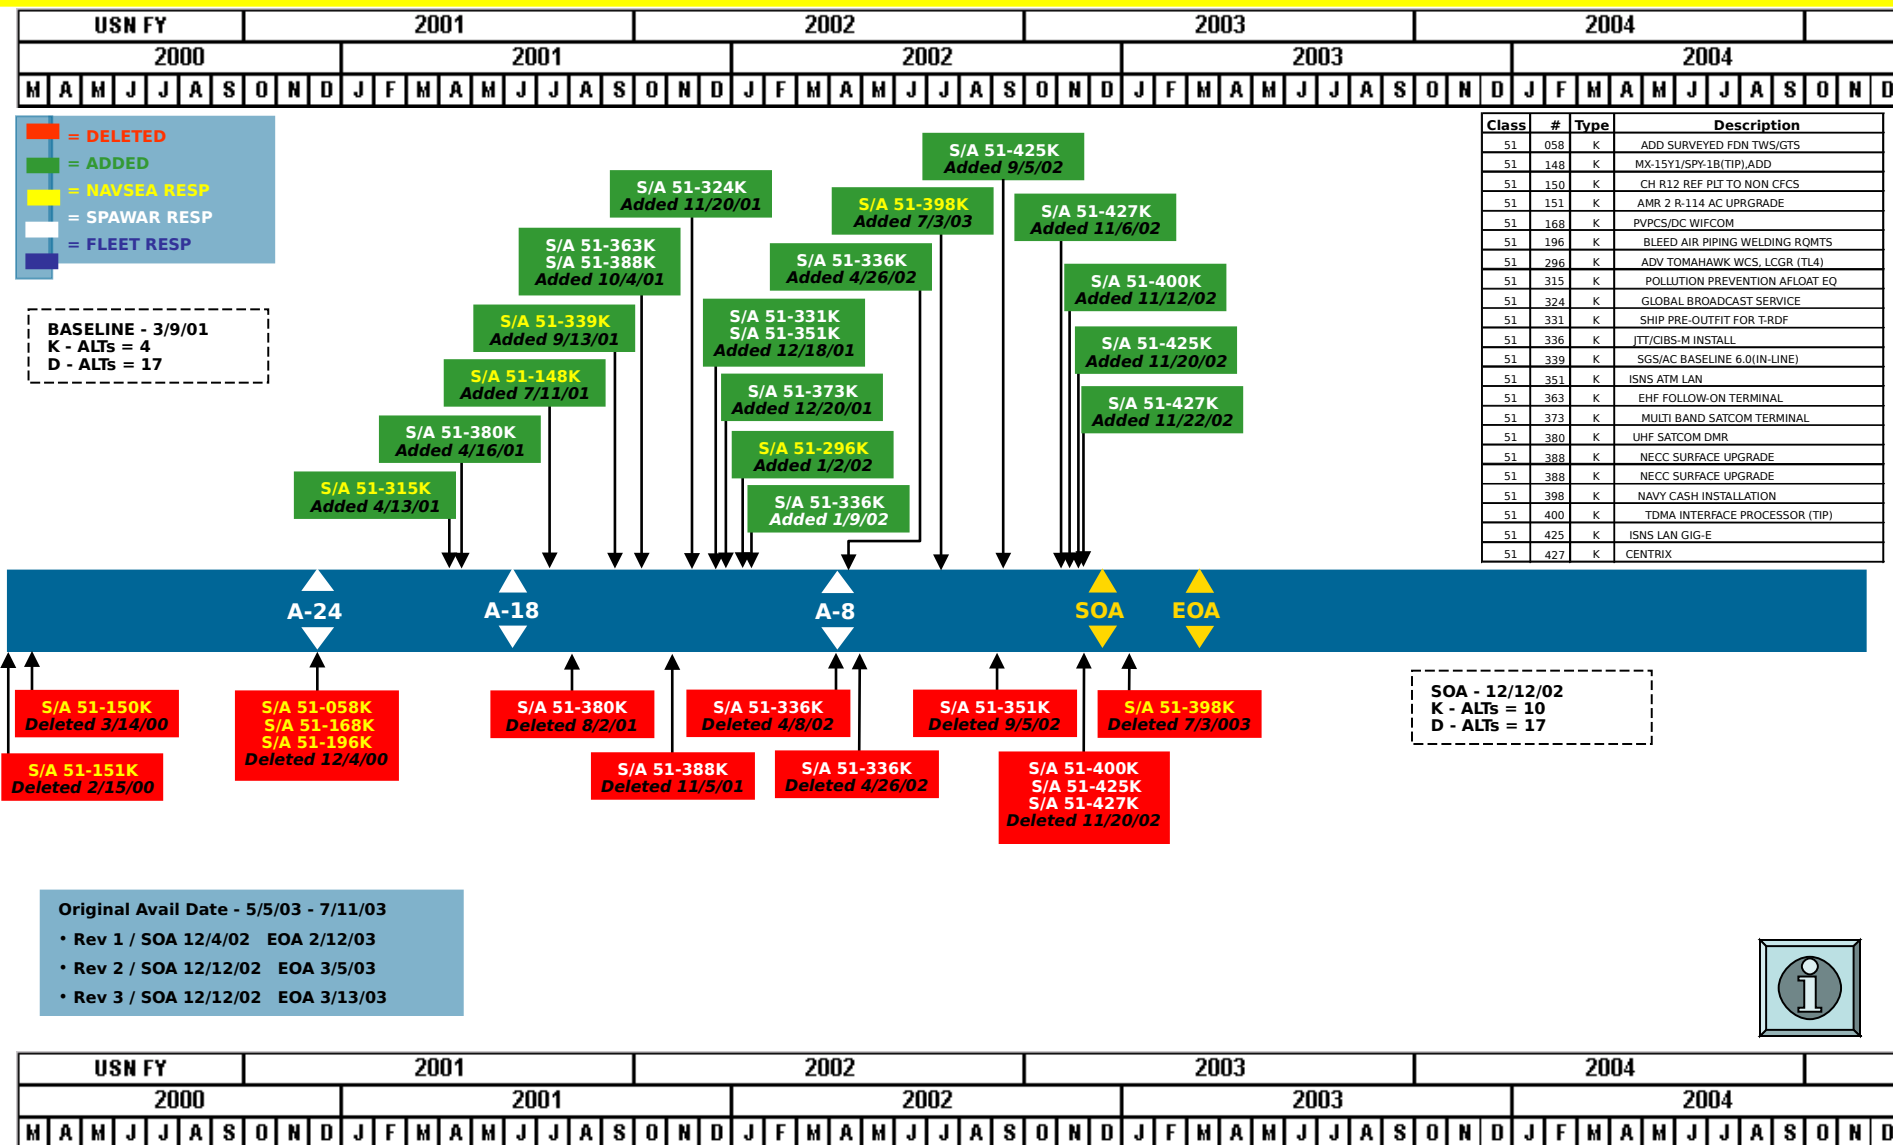



USS JOHN PAUL JONES (DDG 53)

DSRA 5

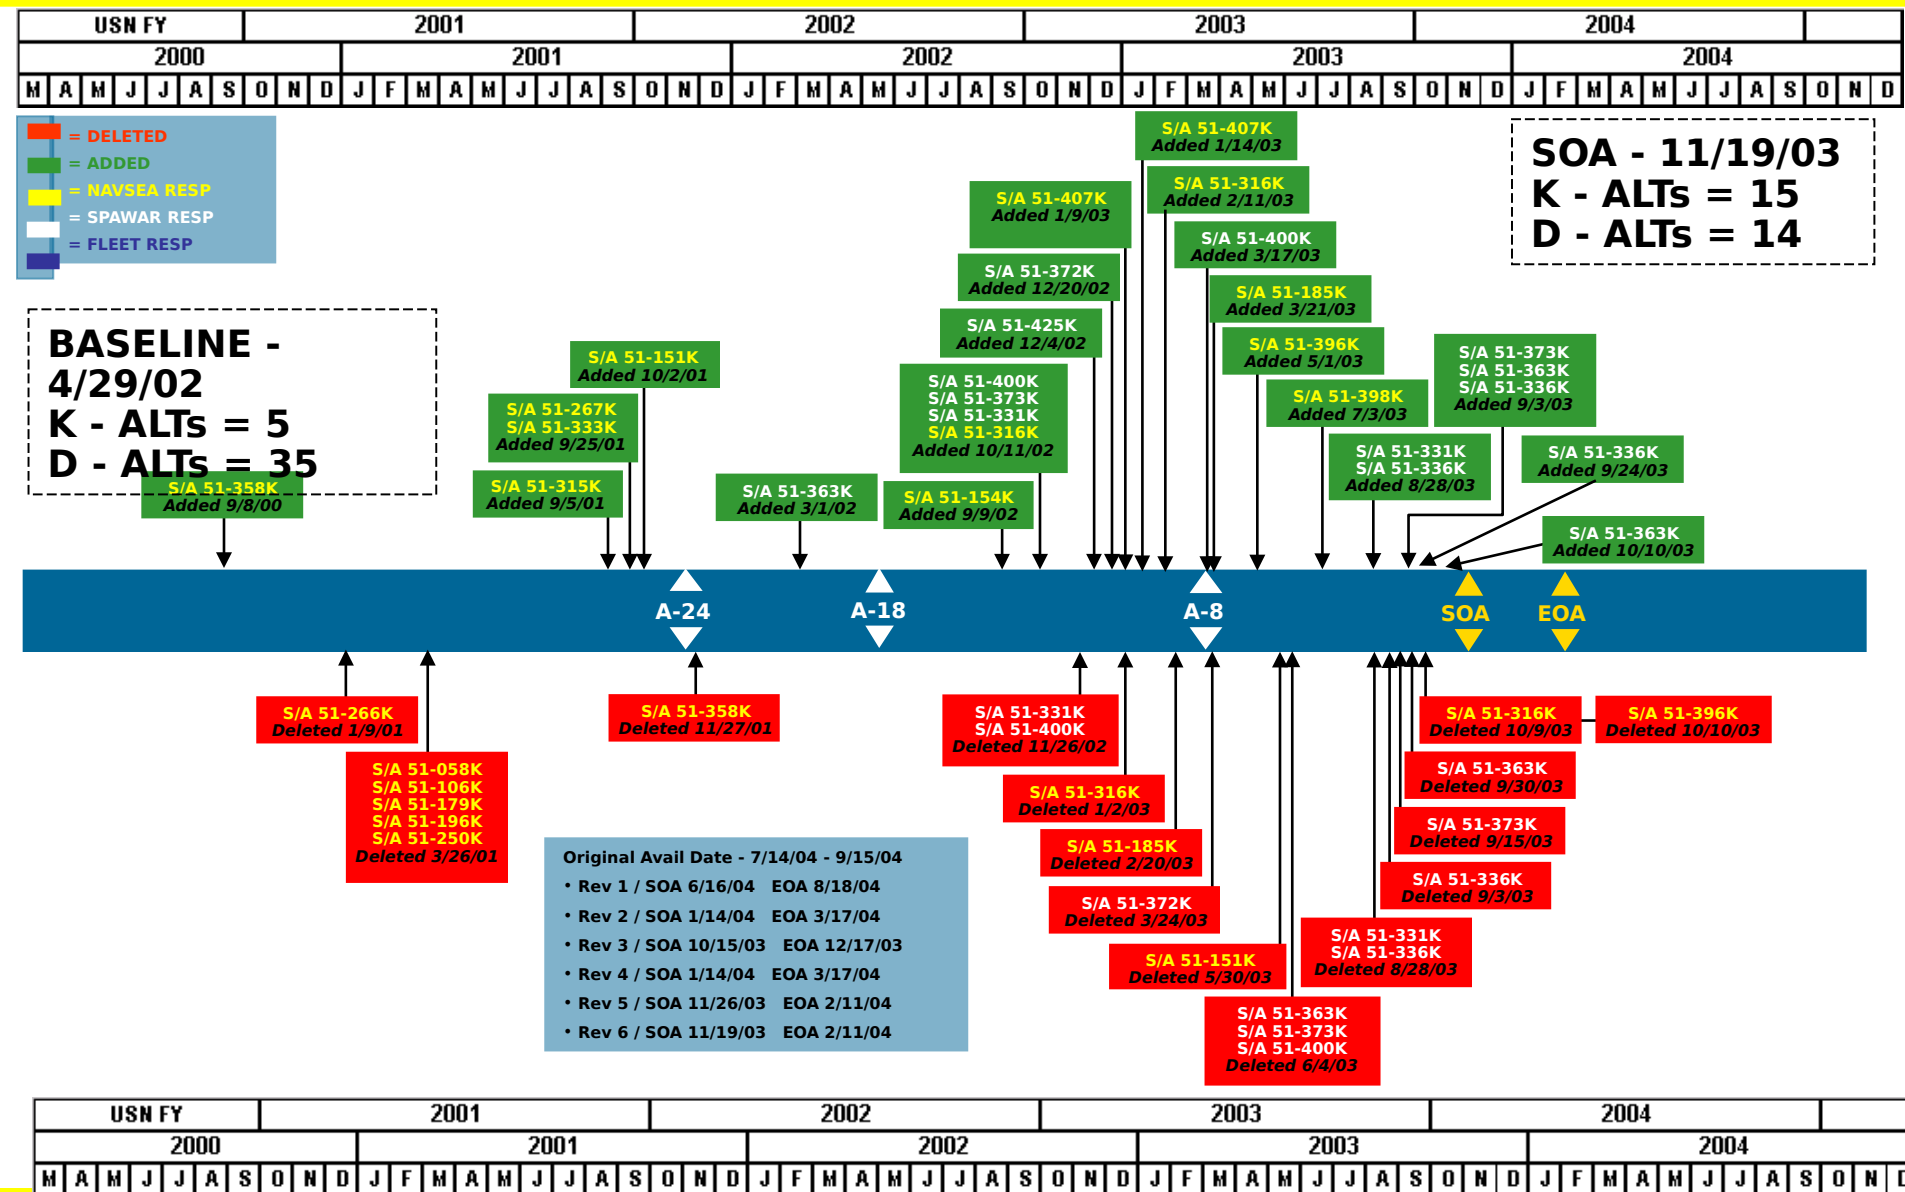


Definition of Churn:

Additions and deletions to the ship modernization package after A-12

- **Churn costs money**
- **Churn impacts availability schedule and execution**

- **Unable to participate in Shipcheck at A-11/12**
 - *Shipcheck location may change to overseas*
 - *May decide not to Shipcheck*
- **Churn disturbs work sequencing in planning**
 - *SID generation*
 - *Late/incomplete ICD's*
- **Churn disturbs work sequencing during execution**
 - *Integration of services*
 - *Amendments to existing SOW's*
 - *Impacts upon test schedules*
 - *New crew training requirements*
- **Equipment frequently requires increased shipping costs**


Milestones



- **Issue Advanced Planning Letter (APL)** **A-18**
- **Issue Authorization Letter (LOA)*** **A-12**
- **Task & fund SID development*** **A-11**
- **Complete shipchecks** **A-9**
- **Issue SIDS to NSA*** **A-6**

***Proposed SHIPMAIN Milestones**


Milestones



- **Provide funds for ordering LLTM*** **A-6**
- **Provide availability funding*** **A-5**
- **Provide identification of ALT support services*** **A-4.5**
- **ILS Certification plan approved*** **A-4**


***Proposed SHIPMAIN Milestones**

Adding a Late Shipalt



- **Is there adequate time to develop a Planning Yard Design for the ship?**
- **Will all equipment/material support Start of Avail (SOA) dates?**
 - **If not, will material arrival permit install and testing to complete prior to end of availability (EOA)?**
 - **Will late material compromise quality of the AIT Team installation?**

PARM Fielding Plans



- **For existing ShipAlts: Deliver by end of each odd numbered month**
- **For new ShipAlts or when major re-rack of existing ShipAlts: Deliver when 1st available**
- **Include:**
 - **Description of changes**
 - **ShipAlt # for each class**
 - **Full name of program, plus common names**
 - **PARM name and contact information plus back up POC information**
 - **Request PARMs populate NDE-NM for each class ship**
- **Deliver to: Georgia Cylke at: cylkegl@navsea.navy.mil**

- **Update NDE scheduling information**
 - Enter scheduling information in NDE
 - AIPS for outside CNO avail window installations
- **Send budgeting updates to SHIPS-FP**
 - Ensure NC-50s are complete, up to date and that the correct data is reflected
- **NDE Account information**
 - <https://www.nde.navy.mil/>
- **Questions contact Georgia Cylke at (202) 781-0521**
